

Course: Individual Software Development Process' 2026

Iteration Report: Iteration 1

By UnpaidInternship

Chosen Irl Challenge: Project C: Department Information & Communication Hub



Chutikarn Stenger	6810545573
Dhechid Phumpaka	6810545603
Varissara Arayavilaipong	6810545891
Wiran Watanathira-anan	6810545913

Table of Contents

1. Project Snapshot.....	1
1.1 Project-Wide Gantt Chart.....	1
1.2 Current Iteration Gantt Chart.....	1
2. Sprint/Board Status Snapshot.....	1
3. Scope Addition/Change Log.....	2
4. Retrospective.....	2
5. Testing & Quality Notes.....	2
6. Project Risk Register.....	3
7. Individual Contribution Log.....	3


1. Project Snapshot

Note: This section must include both Gantt Chart for the whole project and the calculation of the critical path for the project, and each iteration. Created via Plane.so.

Note: Project Repository is mandatory for the report submission of Iteration 2. For Iteration 1, this can leave blank as "(WIP)".

Project Repository: <https://github.com/Khaomi/prototype-101/>


1.1 Project-Wide Gantt Chart

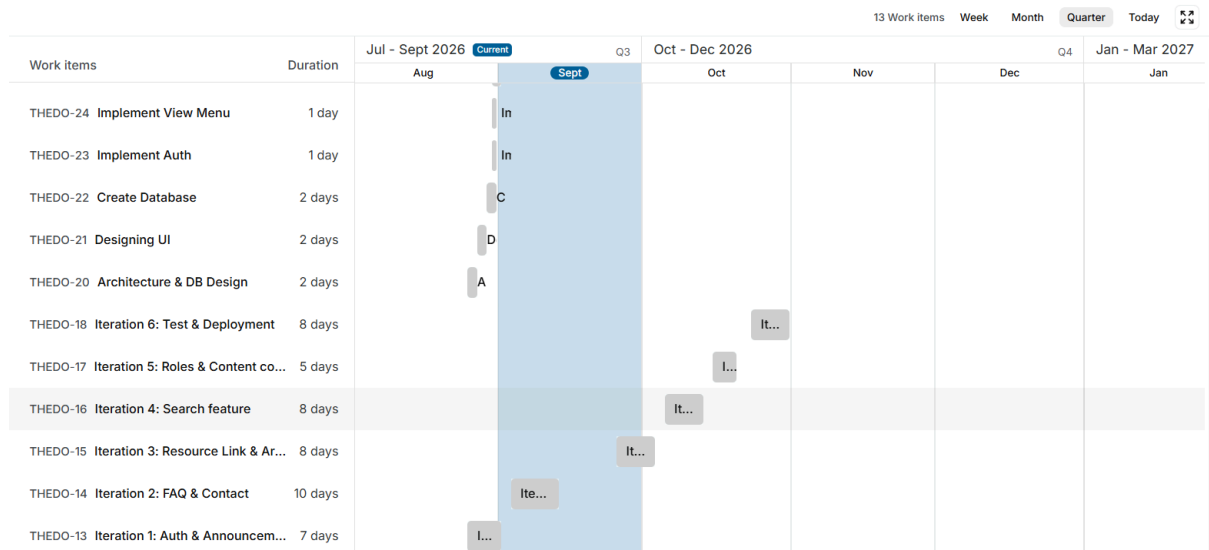

Critical Path: Iteration 1: Auth & Announcement → Iteration 2: FAQ & Contact → Iteration 3: Resource Link & Archive flow → Iteration 4: Search feature → Iteration 5: Roles & Content control → Iteration 6: Test & Deployment

Critical Path Duration: 66 calendar days

1.2 Current Iteration Gantt Chart

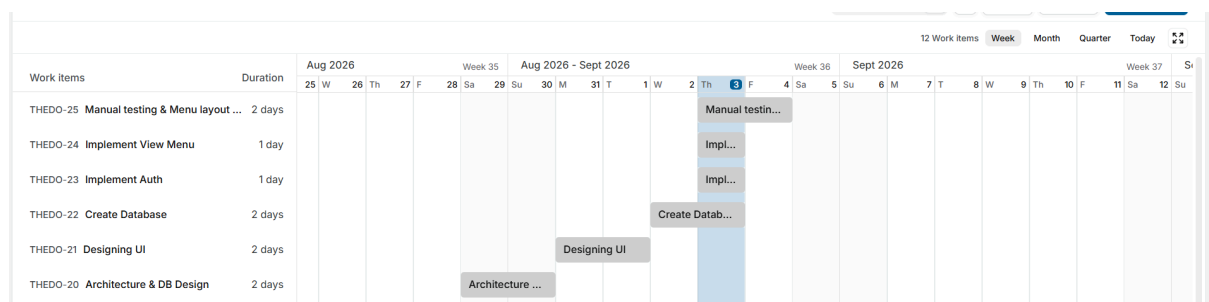

Critical Path: Architecture & DB Design → Designing UI → Create Database → Implement Auth → Implement View Menu → Manual testing & Menu layout fixing

Critical Path Duration: 7 calendar days

2. Sprint/Board Status Snapshot

Note: User Stories Must Be Consistent User Stories in Software Proposal (Week 4). For Maximum Capacity, It Must Be:

- 3 User Stories for Iteration 1
- 4 User Stories for Iteration 2

Iteration Goal: Deliver a working, doable slice where an authenticated department member can log in via Google (@ku.th) and view current announcements, while an authorised staff/TA member can create a new announcement which directly supporting Sub-Goals SG-1 (current information access), SG-2 (complete content details), SG-3 (authorised updates), and SG-8 (restricted access) from the SRS.

Capacity Declared: 3 user stories (at the Iteration 1 hard limit; no basis needed as this is the fixed ceiling for a first iteration).

User Story	Description	Owner	Status	Within Capacity (Y/N)	Notes
US-15	As a user, I want to log in with my department Google account so I can access the system securely	Dhechid Phumpaka	Done	Y	Core blocker task; every other story depended on this being completed first, so it was prioritised ahead of schedule. Verified working with @ku.th emails accepted and other domains rejected (SRS-13).
US-1	As a student, I want to view current announcements so I don't miss updates	Varissara Arayavilaipong	In Progress	Y	Front-end built against mock data; layout still under review by group members suggested that a single-column list is easier to read than the grid currently implemented,

					so this is being weighed before finalising. Not yet connected to the live database.
US-3	As staff/TA, I want to create/edit an announcement	Varissara Arayavilaipong	In Progress	Y	Blocked on the database schema being finalised first, since form fields and validation must match the schema exactly. Schema is now complete; form UI implementation is the next step.

3. Scope Addition/Change Log

Note: Log any item added, expanded, or swapped in after planning began. Empty is a good sign; frequent entries signal scope creep.

Item added/changed	Reason	What as dropped to compensate (one-in-one-out)
(None applicable)	Team stayed within the originally committed 3 user stories (US-15, US-1, US-6) for the iteration	(None)

4. Retrospective

What went well	What didn't go well	Action items for next sprint
The SRS and data model were fully finalised prior to development, which meant	The majority of the team was learning TypeScript concurrently with	Establish a shared reference of common TypeScript patterns before Iteration 2

no scope renegotiation was required mid-sprint.	implementation, which extended the time required for both US-1 and US-6.	begins, reducing time spent looking up syntax mid-task.
US-15, identified as the highest-risk item this iteration, was completed and verified as fully functional.	US-6 could not proceed until the database schema was finalised, a sequencing dependency that was not accounted for during sprint planning.	Sequence dependent tasks explicitly during planning schema work ahead of form implementation rather than scheduling them in parallel.
-	The declared capacity of 3 stories was reasonable under the course's constraints, but the team underestimated the time required for TypeScript-heavy frontend work, given the team's lack of prior experience with it.	Allocate a larger time buffer for any task involving unfamiliar tools or techniques.

5. Testing & Quality Notes

Note: any bugs, defects, tests (informal & formal) encountered and/or fixed during this iteration can be included here. If there is none, just put "(None applicable)" below.

Tests performed	Defect found	Fix applied
Manually tested the announcement UI with mock data: the grid layout renders correctly, clicking a card opens the full detail view, and the back button correctly returns to the previous page.	The filter panel's Activity group was defaulting to open on every page load, while all other filter groups (Year, Course, For who) defaulted to closed an inconsistent default state	Reset the initial state so every filter group, including Activity, defaults to closed
Test the authentication flow to see if the system correctly redirect the user to the correct page based on what account is selected	The authentication system fails to redirect to the correct URL	Add the correct URL to the list of allowed redirect URL inside the Supabase's dashboard

6. Project Risk Register

Risk ID	Description	Likelihood (L/M/H)	Impact (L/M/H)	Mitigation/Contingency	Status
R-01	The grid vs. list layout decision	M	M	Set a hard decision deadline	Open

	for announcements is still unresolved; delaying it further could block US-1 from reaching Done			before Iteration 2 planning begins, based on the tester feedback already collected	
R-02	Only Dhecid has hands-on OAuth/NextAuth experience — a single point of failure if auth needs debugging later	M	H	Document the auth setup clearly and walk another team member through it during Iteration 2	Open
R-03	Team has no prior experience, so future self-declared capacity may be miscalibrated the same way US-15's estimate was	M	M	Track actual time spent per story this iteration to build a velocity baseline for Iteration 2 planning	Monitoring

7. Individual Contribution Log

Note: One row per member, filled in by that member. The submission of this file considered that the form below is consented and confirmed by the whole team. This section directly supports the Individual Project Contribution and Peer Evaluation grading components.

Note 2: For Iteration 1, evidence can be a reference to the video presentation/iteration report that is related to the responsible task(s) (e.g. Lalita's Evidence). However, for Iteration 2, the reference must be on **GitHub file and commit only, which is uploaded by that team member**.

Student Name	Tasks owned this sprint	Course concept(s) applied	Evidence	Self-rated effort (1-5)
Chutikarn	Proposal Diagram	Requirements engineering principles	proposal	2
Varissara Arayavilaipong	Proposal, Figma design, Report, Front-end implementation for US-1 (View Announcements)	Applied US-1 and US-6 with CRUD method	In presentation video, Github, MockUp Website	4

	) and Video Edit			
Wiran Watanathira-anan	- Proposal Diagram - Report gantt chart - Video Editor	Applied Gantt chart method from the first class	proposal, Iteration 1 report, Presentation video	2
Dhechid Phumpaka	US-15 (User authentication system)	Applied US-15	Presentation video, GitHub, Public Website	4
